



**English follows.**


## Mise à jour de la semaine 11 pour le projet de la rue Main

### Travaux achevés la semaine dernière

- Bordures et trottoirs sur les rues Main et Dock.
- Mise en place de 0-31,5 mm sur la rue Main.
- Installation des poteaux d'Énergie NB.
- Test des égouts et vidéo.
- Amélioration de l'accès piétonnier sur la rue Main.

### Travaux prévus cette semaine

- Base d'asphalte pour le côté sud de la rue Main et de la rue Dock.
- Réparations à partir de l'évaluation vidéo des égouts.
- Trottoirs.
- Valve d'isolation sur la rue Winter le mercredi 31 juillet qui nécessitera une journée de fermeture de l'eau.

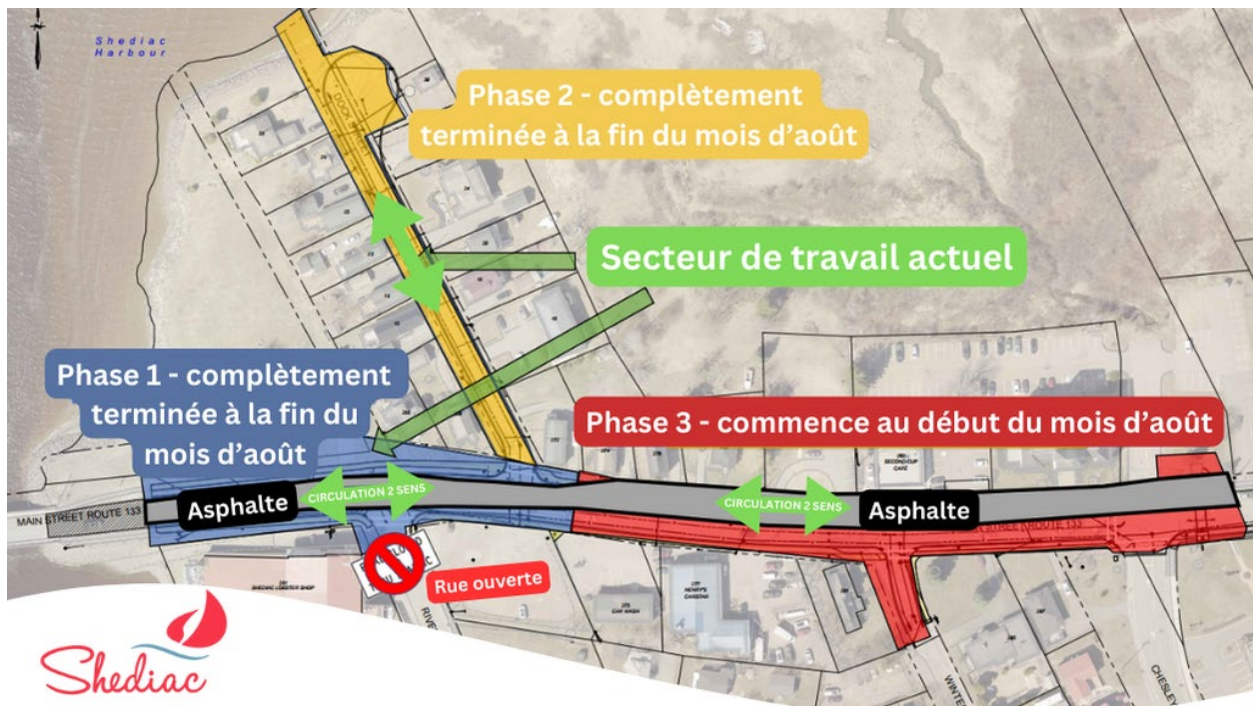



## Week 11 update for the Main Street project

### Work completed last week

- Curbs/sidewalks on Main and Dock Street.
- 0-31.5 mm placement on Main Street.
- NB Power poles installed.
- Sewer testing and video.
- Improve pedestrian access through Main Street.

### Planned work for this week

- Asphalt base for south side of Main and Dock Street.
- Repairs from sewer video report.
- Sidewalks.
- Isolation valve on Winter Street Wednesday, July 31 that will require a day water shut down.

